DANSANI
DANISH BATHROOM DESIGN

ORDER FORM

CALIDRIS MTM WALL-HUNG UNIQUE BASINS

Customer:	Required supply date: (min. 6 weeks)	Order no./Ref.:
Contact person:	Order date:	Order no. Dansani: (added by Dansani)

Silestone® decor *See available colours on our website*		*NB: See our website for specific lead time*	
Tap hole	○ With tap hole	○ Without tap hole	○ For 3 hole tap
Depth	○ 505 mm	○ * _____ mm	*NB: Max 605 mm* **only fill out for bespoke depth*
Height	125 mm - standard skirt height		
Size of basin	○ Small: 500 x 300 mm *NB: for all sizes of vanity units*	○ Large: 650 x 300 mm *NB: for vanity units with a width of 800 mm or more*	

Measurements

Width
NB: Small - min 740, max 2405 mm
Large - min 890, max 2405 mm

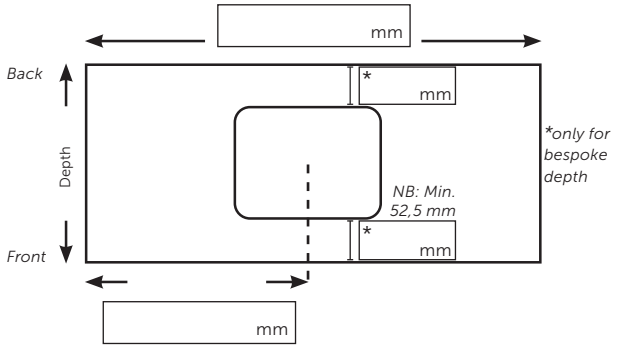

From the edge to centre of the waste
NB: Small - min 370 mm
Large - min 445 mm

Width
NB: Small - min 1340, max 2405 mm
Large - min 1640, max 2405 mm

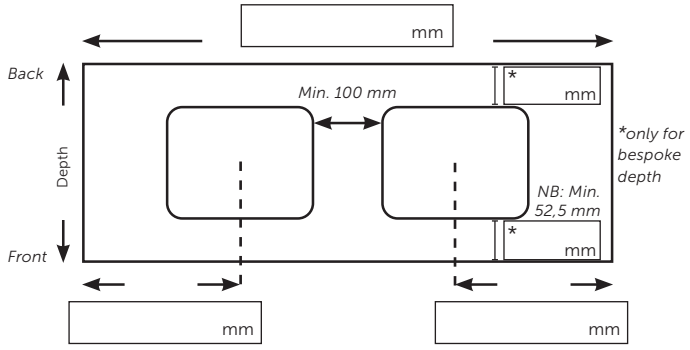

From the edge to centre of the waste
NB: Small - min 370 mm
Large - min 445 mm

From the edge to centre of the waste
NB: Small - min 370 mm
Large - min 445 mm

Accessories at additional cost - see catalogue for prices

Concealed overflow kit *NB: not for D405 mm*		☐ Chrome Art. no. 4893843-3	Basin waste continuous flow		☐ Chrome Art. no. 4883143
Basin waste with automatic opening		○ Chrome Art. no. 4884343	○ Polished brass Art. no. 4884344	○ White matt Art. no. 4884310	○ Black Art. no. 4884328

NB:

- Required basin support bracket for installation on wall included
- The basins have a tolerance of +1/-1 mm; we recommend that all basins are ordered 5 mm wider than the furniture setting (e.g. 1605 mm total width to suit 2 x 800 mm units).
- If the basin is placed on a vanity unit, the centre of the basin must be aligned with the centre of the vanity unit.
- For wall-to-wall solutions we recommend 3 mm space on both sides between worktop and wall. Take care to note the diagonal measurement between the walls.
- Bespoke products cannot be cancelled or returned after the signed order form is received.
- Please be aware that the warranty no longer applies if modifications to the construction and/or the design are carried out.

Signature of acceptance Name/Company stamp

141125. Rev. 01
